State University Construction Fund

SUCF PROJECT NO. 161026-04
RENOVATE PLANT SCIENCE BUILDING

PHASE I

MWBE/EEO OVERVIEW REPORT

OCTOBER - DECEMBER 2025

2/20/2026

DACK CONSULTING SOLUTIONS, INC

TABLE OF CONTENTS

1. EXECUTIVE SUMMARY 1
2. GOALS 2
3. OUTREACH 3
4. MWBE/SDVOB COMPLIANCE 4
5. MWBE/SDVOB PAYMENTS..... 6
6. WORKFORCE DIVERSITY 10
ATTACHMENT A 14
ATTACHMENT B 17

1.EXECUTIVE SUMMARY

The State University Construction Fund ("SUCF, Fund"), LeChase Construction ("LeChase"), Owner's Representative, and FAHS Construction Group, Inc. ("FAHS"), General Contractor, have remained committed to working with Minority, Women and Service Disabled Veteran-owned ("MBE, WBE and SDVOB") businesses and fostering a diverse workforce throughout the Plant Science Building Renovation Project (Phase 1) at the New York State College of Agriculture and Life Sciences at Cornell University. As the project approaches final completion, the team continues to uphold these commitments through project closeout.

The scope of work included a phased gut renovation of the main building program spaces, incorporating new floor plan layouts; installation of new mechanical, electrical, plumbing, and fire protection systems; abatement of hazardous materials; window replacement; elevator upgrades; and improvements to the building's thermal and energy performance. The construction cost, based on the GC's base contract, was $49,339,000 with a $2,021,000 allowance. The project was awarded to FAHS in March 2023, and Phase I is on track for completion in December 2025.

The Fund's initial project goals were 15% MBE, 15% WBE, and 6% SDVOB participation. While a waiver was granted by the Fund in recognition of the demonstrated good-faith efforts, the approved participation levels reflect commitments of 7.76% MBE, 10.58% WBE, and 0.3% SDVOB.

Although no specific workforce diversity percentages were mandated, the Fund required the GC to electronically report Equal Employment Opportunity (EEO) workforce data and track workforce diversity throughout the project. This reporting has been maintained through the final phases of construction.

To support, track, and monitor these goals, DACK Consulting Solutions, Inc. ("DACK"), a subconsultant to LeChase, served as the Project's MWBE Consultant in partnership with the project stakeholders through substantial completion.

As of December 2025, and inclusive of change orders, the total contract value awarded to MWBE and SDVOB firms increased to $10,131,180 with $9,514,434 eligible toward goal attainment (reflecting the 60% supplier credit). This represents over 18.4% of the total contracts awarded on the project.

Significant progress has also been made in payments to MWBE firms. As of December 2025, $7,881,522 —approximately 77.8% of the total awarded value to MWBE/SDVOB firms—has been disbursed. Final payments are anticipated to be processed in alignment with project closeout activities.

As the project concludes, the team remains committed to supporting diversity and inclusion through final reporting and closeout, ensuring all participation and compliance requirements are fully documented and satisfied.

2. GOALS

The Fund initially set **project-specific participation goals** of **15% Minority Business Enterprise (MBE), 15% Women Business Enterprise (WBE), and 6% Service-Disabled Veteran-Owned Business (SDVOB).** These goals were established to promote diversity and equitable access to contracting opportunities on the project.

However, after an extensive review of the efforts made to engage and contract MWBE and SDVOB firms, **the Fund granted a waiver and approved a revised utilization plan** that more accurately reflects the availability and capacity of qualified firms in the marketplace.

- **MBE:** 7.76% (down from 15%)
- **WBE:** 10.58% (down from 15%)
- **SDVOB:** 0.3% (down from 6%)

While the revised individual category goals have been adjusted, the overall **combined MWBE utilization goal remains strong, exceeding 18%**. This figure reflects the total engagement of certified MWBE firms across different contract categories, ensuring meaningful participation despite the waiver.

DACK played a crucial role in **documenting, verifying, and justifying** the waiver request by demonstrating **good-faith efforts** to secure MWBE and SDVOB participation. This included:

- **Conducting outreach efforts** to identify and engage eligible MWBE/SDVOB firms.
- **Monitoring contract awards** to ensure MWBE firms were given equitable opportunities.
- **Reviewing utilization plans** submitted by prime contractors and assessing their compliance.
- **Tracking payments** to confirm that MWBE and SDVOB firms were compensated according to contractual agreements.

Although the revised targets are lower than the initial goals, the Fund's approval indicates that **DACK and project stakeholders made sufficient and documented efforts** to meet the original objectives. The waiver approval demonstrates an acknowledgment of the realities of subcontractor availability and reinforces the commitment to **achieving the highest feasible MWBE and SDVOB participation.**

By maintaining transparency and compliance, **DACK ensures that MWBE and SDVOB engagement remains a priority**, contributing to an inclusive and equitable procurement process for the project.

3. OUTREACH

To increase participation of MWBE/SDVOB firms in the project, DACK provided outreach during the bidding phase. DACK uses a variety of methods to engage the MWBE community. We create informational e-blasts providing project details; post on social media about the event; partner with organizations, chambers, and state & civic organizations; develop master lists of contractors to target for the project; develop a central email portal (MWBEOutreach@dackconsulting.com) to process all the MWBE contracting interests; organize and coordinate Information Sessions to inform contractors about current and up-coming bidding opportunities.

In order to maximize the reach to MWBE community, DACK and LeChase held 2 events during the bidding phase: In-person Walk-through Outreach and Virtual Meeting Outreach. No outreach events were held this Quarter.

4. MWBE/SDVOB COMPLIANCE

As the MWBE/EEO Consultant for the Project, DACK plays a critical role in supporting and monitoring compliance with Minority- and Women-Owned Business Enterprise (MWBE) and Service-Disabled Veteran-Owned Business (SDVOB) goals. A key component of DACK's responsibilities includes MWBE Compliance Monitoring, which entails reviewing awarded contracts and assessing whether MWBE firms are being utilized in accordance with established requirements.

DACK evaluates both the MWBE Utilization Plans submitted by prime contractors and the actual contracts awarded to certified MWBE subcontractors and suppliers. This ensures not only that MWBEs are being engaged in a meaningful way, but also that their participation aligns with New York State's (NYS) standards and guidelines.

It's important to note that, per Empire State Development (ESD) regulations, NYS-certified MWBE suppliers coded under construction trades may only receive credit for 60% of any payments received. This credit adjustment reflects the distinction between suppliers and direct service providers or subcontractors, ensuring compliance data accurately represents MWBE participation in the project.

As of December 2025, total awards counted towards the goal to MWBE and SDVOB firms amount to $10,131,180 of total contract amount of $51,694,321.

- MBE Awards: $4,343,203
  - Towards Goal: $4,243,203 with 60% correction for suppliers
- WBE Awards: $5,565,534
  - Towards Goal: $5,048,788 with 60% correction for suppliers
- SDVOB Awards: $222,443
  - Towards Goal: $222,443

MWBE/SDVOB Utilization

Latest as of December 2025

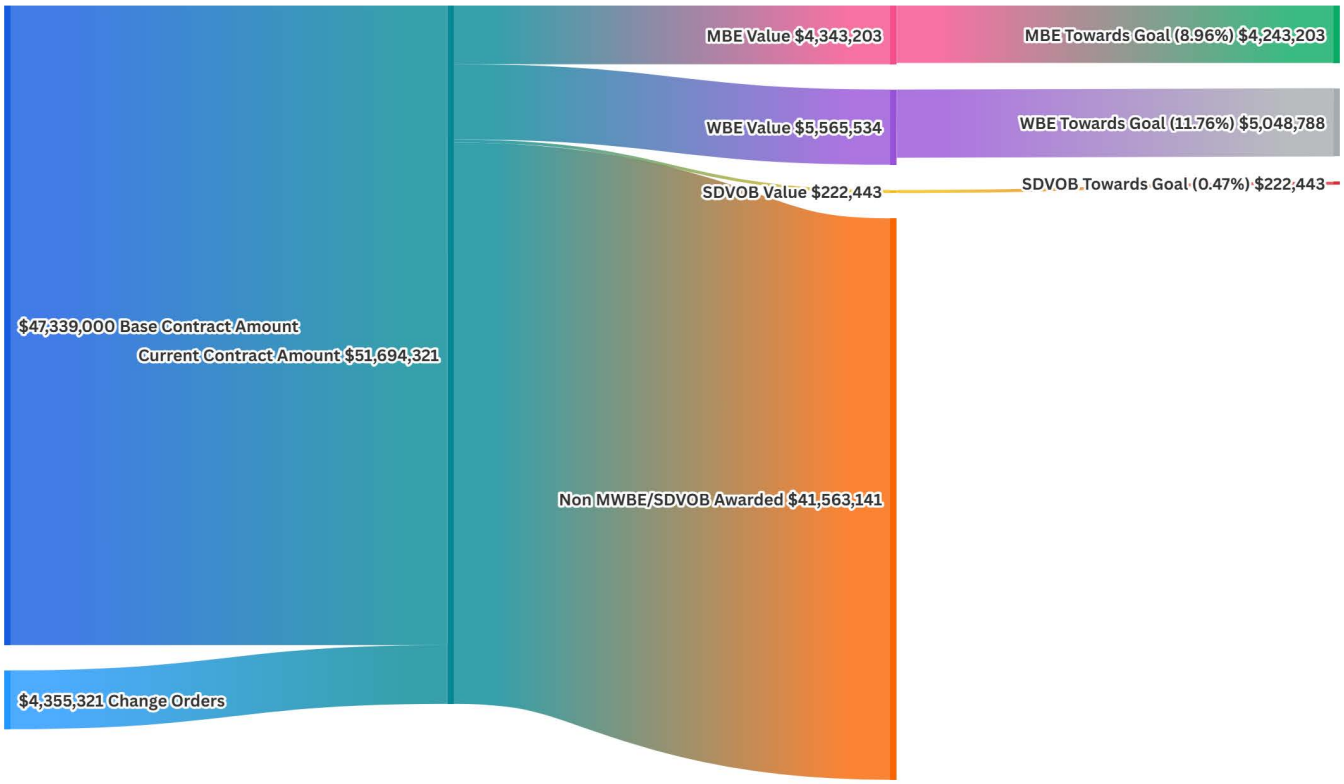

Current Contract Amount: $51,694,321

5. MWBE/SDVOB PAYMENTS

DACK's efforts also included ensuring the payments made to the MWBE/SDVOB subs. DACK reviewed each invoice submitted by the sub each month and checked it against the actual payments being made to them.

The tally of the amount paid to MWBE/SDVOB firms as of Decenber 2025 is $7,881,522 or approximately 77.8% of the total awarded value to MWBE/SDVOB firms.

MBE	VALUE	TOWARDS THE GOAL	PAID TO DATE	PENDING PAYMENT
Dyno Group Inc	$1,194,548	$1,194,548	$1,194,548	$0
Kim Industries Inc	$319,500	$319,500	$303,988	$15,512
Right Price Companies Inc	$250,000	$150,000	$0	$250,000
The Stalwart Development Group	$2,579,155	$2,579,155	$2,551,613	$27,542
MBE Total	**$4,343,203**	**$4,243,203**	**$4,050,149**	**$293,054**
WBE	**VALUE**	**TOWARDS THE GOAL**	**PAID TO DATE**	**PENDING PAYMENT**
A & B Heritage Inc	$8,298	$8,298	$0	$8,298
AAA Reinforcing LLC	$230,000	$230,000	$195,980	$34,020
Avarus Solutions, LLC	$420,315	$420,315	$398,002	$22,313
Bonded Building Materials, Inc.	$280,000	$168,000	$168,000	$112,000
Commercial Material Services Inc	$683,000	$683,000	$0	$683,000
Healthy Glass LLC	$6,500	$6,500	$0	$6,500
Illuminating Expressions Distrib	$576,474	$345,884	$345,884	$230,590
Interstate Steel Sales Inc.	$50,000	$30,000	$29,134	$20,866
Ksp Painting of Syracuse, Ltd.	$504,000	$504,000	$263,801	$240,199
Lupini Construction, Inc.	$2,019,000	$2,019,000	$1,921,526	$97,474
MAC Equipment, LLC	$45,000	$45,000	$0	$45,000
Mechanical Testing Inc.	$62,900	$62,900	$0	$62,900
Riccelli Trucking, Inc.	$80,142	$80,142	$80,142	$0
Rommel Fence LLC	$41,000	$41,000	$35,227	$5,773
Turtle & Hughes Inc.	$385,391	$231,235	$231,235	$154,156
Ziske-Kraftworks Inc.	$173,514	$173,514	$0	$173,514
WBE Total	**$5,565,534**	**$5,048,788**	**$3,668,931**	**$1,896,603**
SDVOB	**VALUE**	**TOWARDS THE GOAL**	**PAID TO DATE**	**PENDING PAYMENT**
Academy Energy	$60,000	$60,000	$0	$60,000
AmBuild Supply, LLC	$2,724	$2,724	$2,723	$1
Shamrock Portable Restrooms, LLC	$19,415	$19,415	$19,415	$0
Tony Baird Electronics, Inc	$140,304	$140,304	$140,304	$0
SDVOB Total	**$222,443**	**$222,443**	**$162,442**	**$60,001**

GRAND TOTAL:	**$10,131,180**	**$9,514,434**	**$7,881,522**	**$2,249,658**

WBE Utilization and Payments to Date

Latest as of December 2025

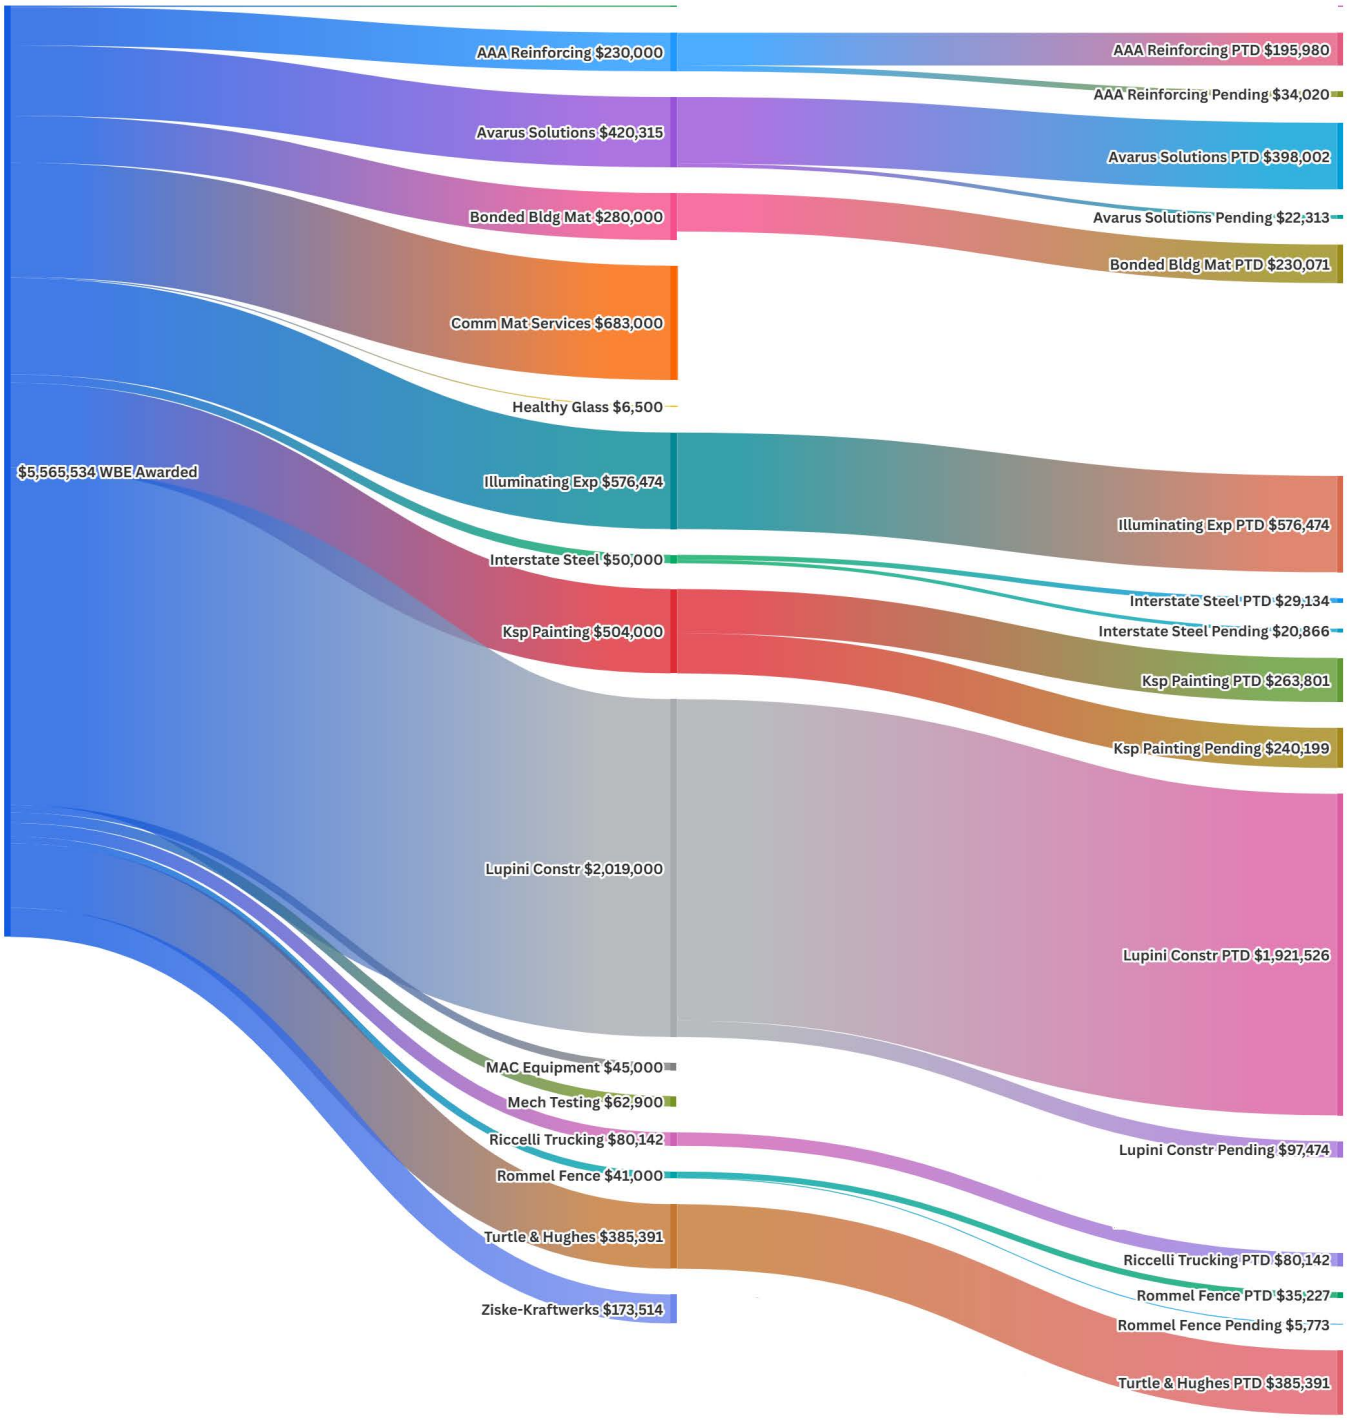

WBE Awarded to Date: $5,565,534

MBE Utilization and Payments to Date

Latest as of December 2025

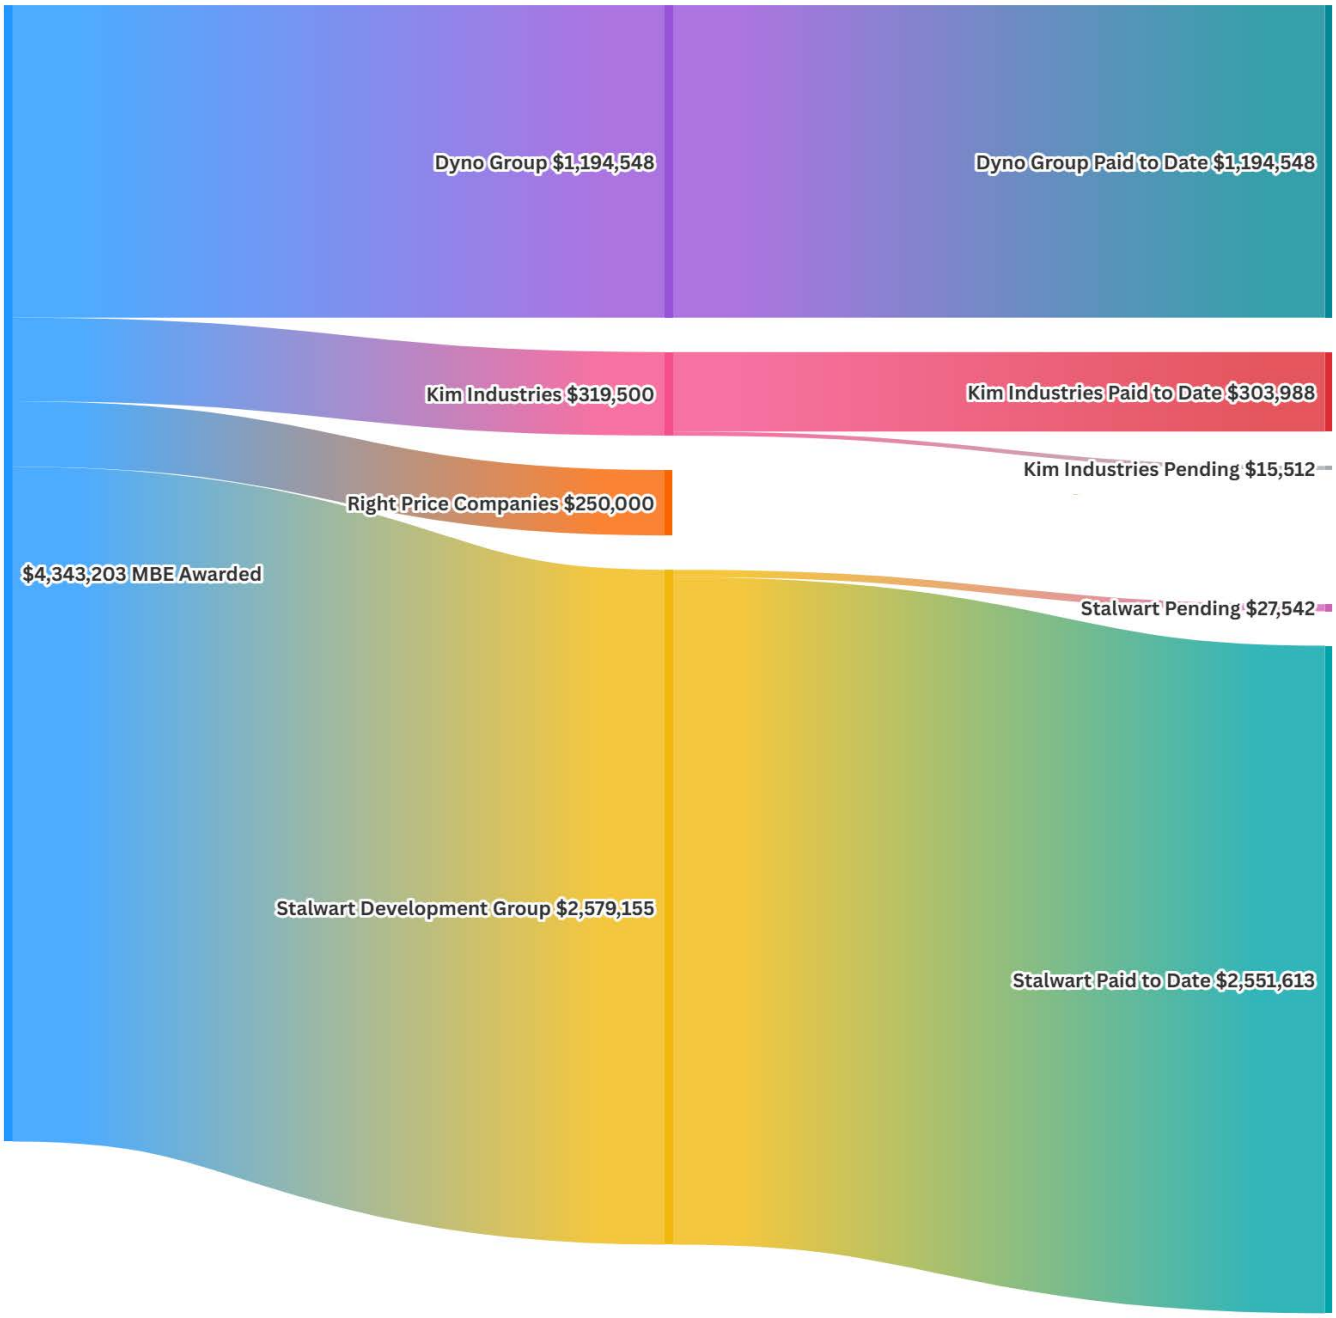

MBE Awarded to Date: $4,343,203

SDVOB Utilization and Payments to Date

Latest as of December 2025

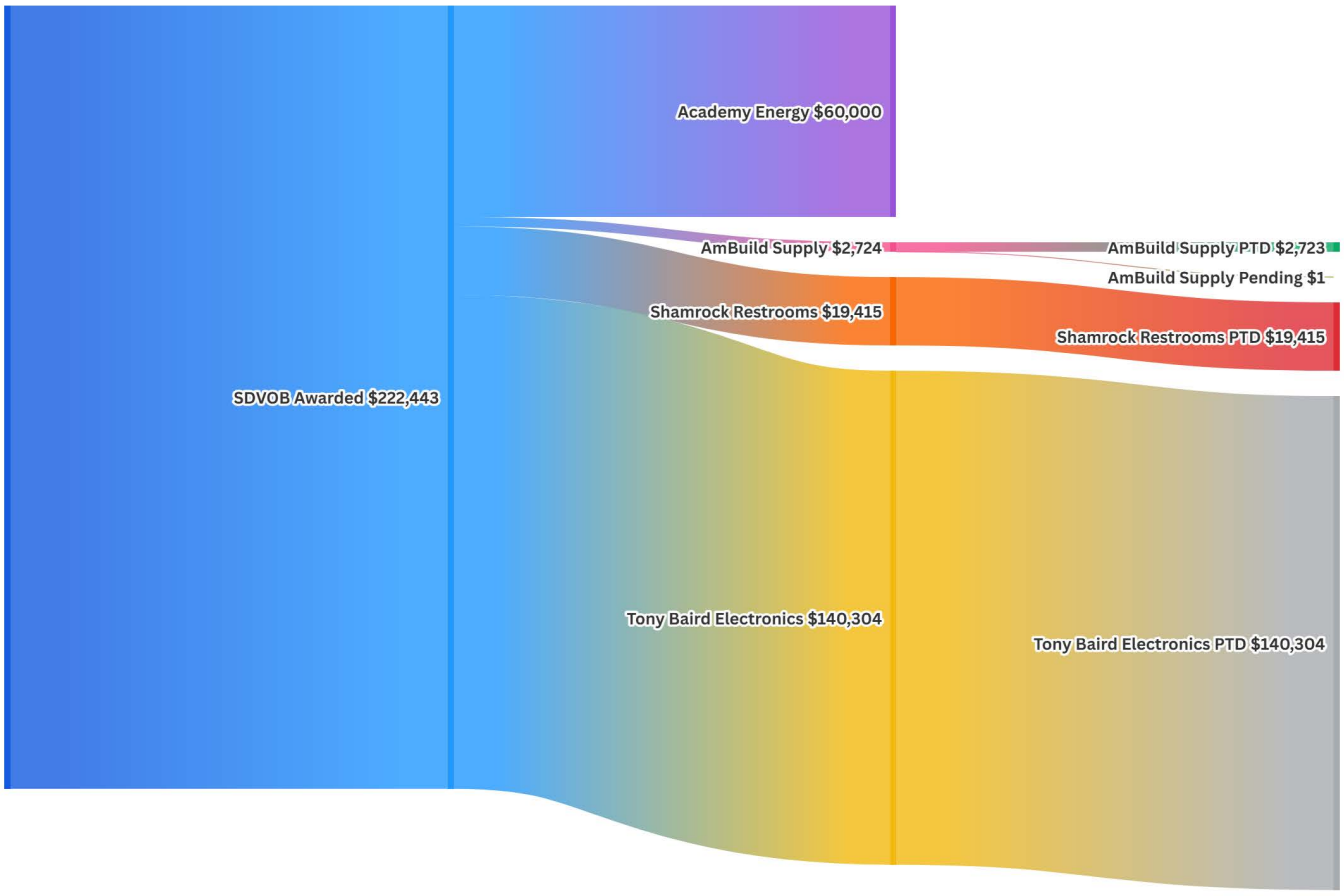

SDVOB Awarded to Date: $222,443

6. WORKFORCE DIVERSITY

SUCF, LeChase, and FAHS are committed to advancing workforce diversity through the implementation of a comprehensive Workforce Diversity Program, supported by policy statements and affirmative action goals. This commitment ensures equal employment opportunities for racial/ethnic minorities and women on the construction site, with a focus on fostering an inclusive work environment. To support this initiative, DD is engaged as LeChase's consultant, providing ongoing guidance and monitoring. This report presents an update on the efforts and outcomes achieved during the third quarter of 2025, reflecting progress toward the program's objectives.

In the Workforce Diversity Program, the hired contractors who assign employees to the sites are informed that they shall take specific affirmative actions to ensure equal employment opportunity. FAHS is committed to maintaining a daily log on-site to ensure compliance, with these log summaries being sent to DACK to maintain records.

DACK meticulously monitored both the number of workers on-site and the hours logged by all workers on site. A detailed spreadsheet was created to record the total hours worked by each employee, based on the data from the daily logs. The information for the third quarter of 2025 is presented, along with cumulative totals.

From October through December 2025, a total of 306 workers were active on the project site (108 in October, 100 in November, and 98 in December).

During this period:

- 8 workers were identified as Black/African American (3 in October, 3 in November, 2 in December).
- 6 workers were identified as Hispanic/Latino (2 each month).
- 6 workers were identified as Native American/Indigenous (2 each month).
- 1 worker was identified as Asian/Pacific Islander (December).
- The majority of the workforce identified as Caucasian/White, with 101 workers in October, 93 in November, and 91 in December.
- Female participation on site included 5 women in October, 4 in November, and 3 in December.

The following pages provide a detailed workforce analysis by minority and non-minority classifications, broken down by subcontractor.

Ethnicity Breakdown by Month per Contractor

Caucasian/White | Black/African American | Hispanic/Latino | Asian/Pacific Islander | Native American/Indigineous

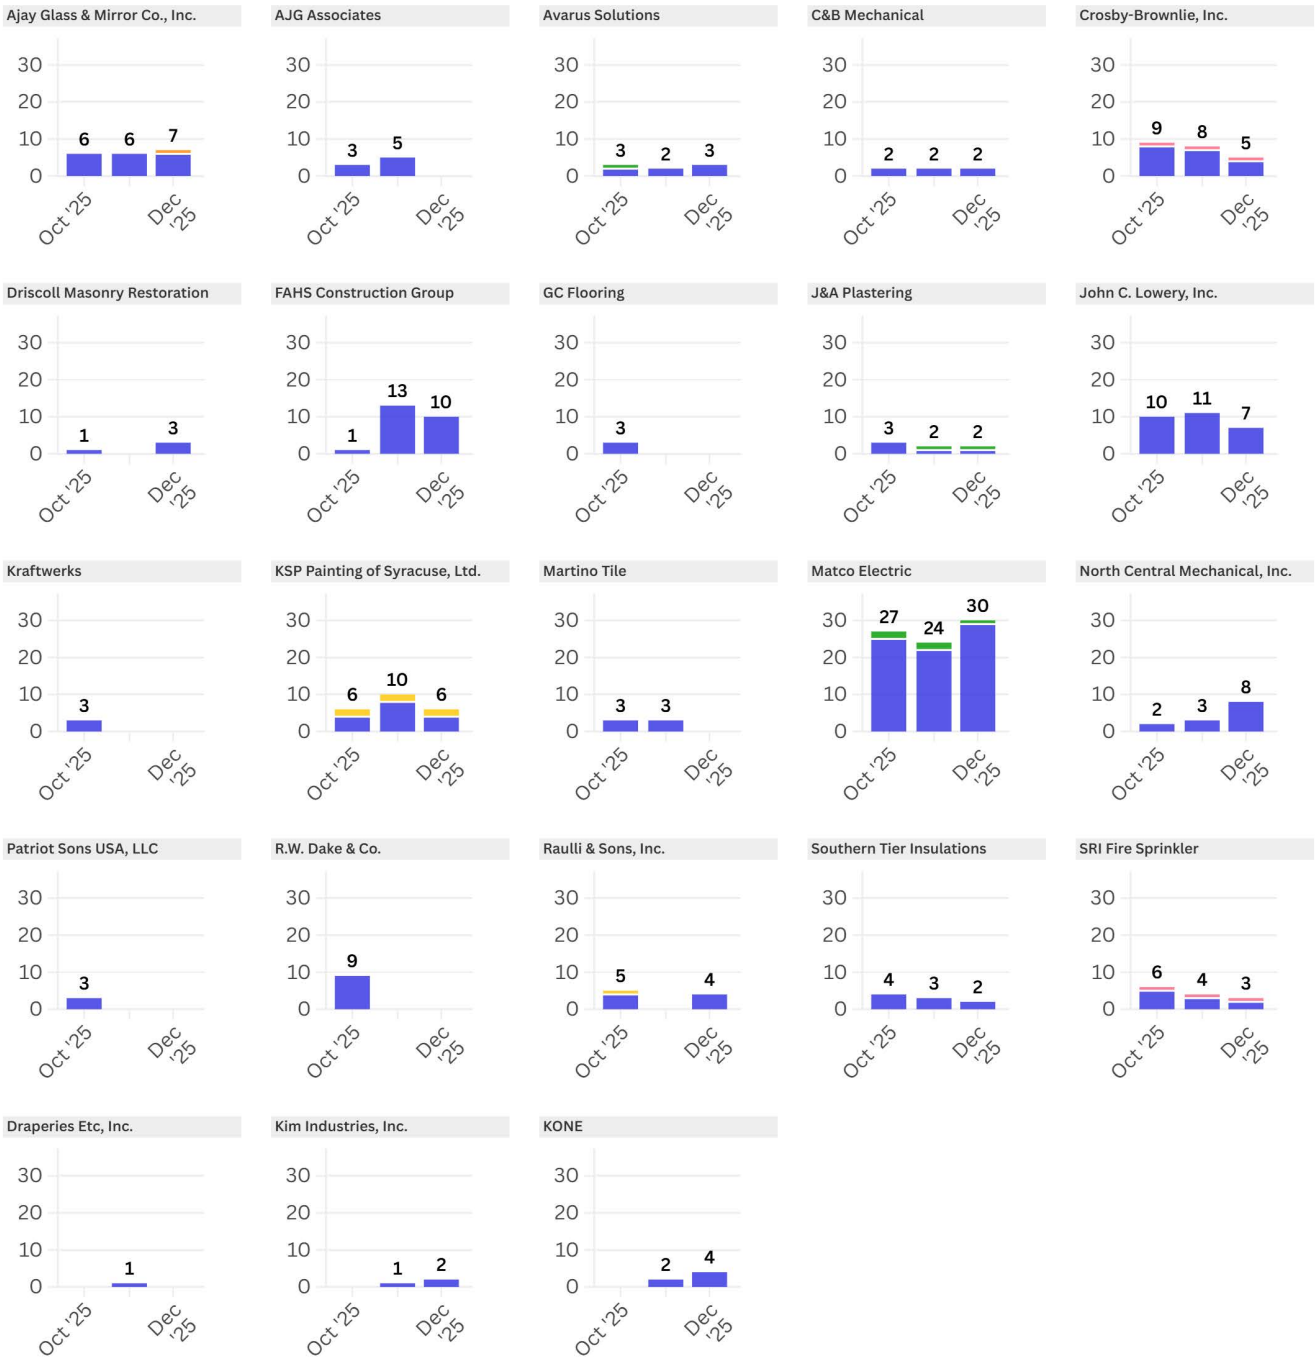

Ethnicity Breakdown by Month

2025 Q4

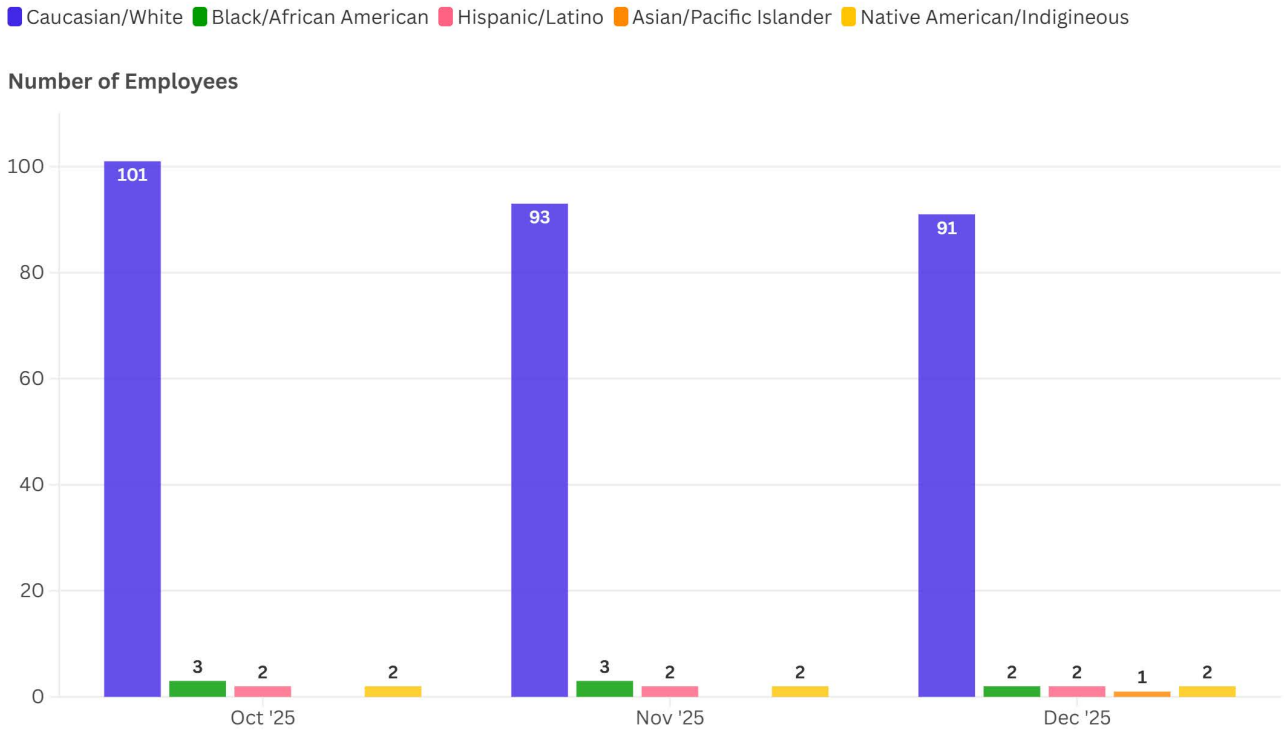

Workforce Breakdown by Ethnicity and Gender

2025 Q4

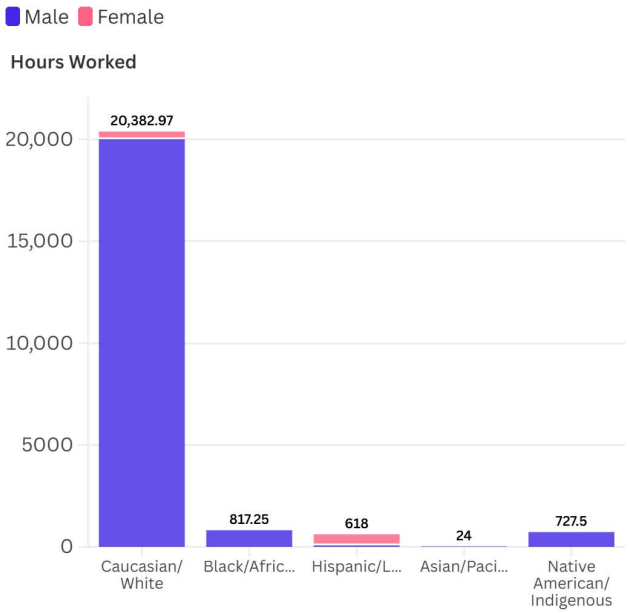

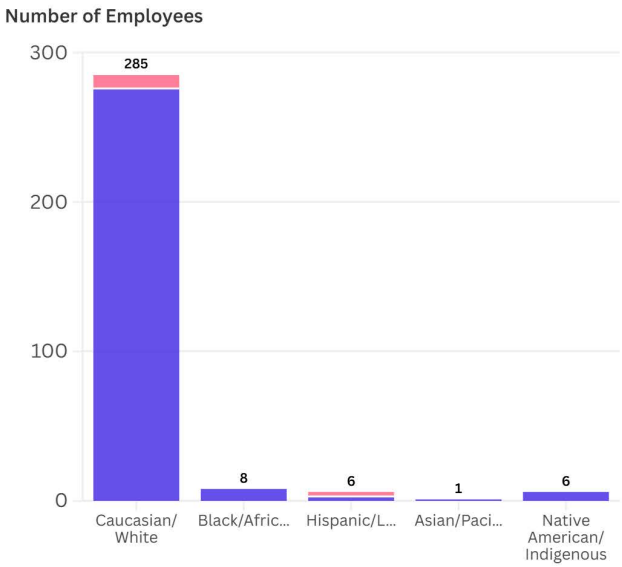

ATTACHMENT A

PAYMENT DETAILS

MWBE/SDVOB Subcontractors Report by Contract

Contract Number:	**D006822**	**Construction Award:**	**$47,339,000.00**	**Payment Application No.:**	**27**
Project Number:	**161026-04**	**Contract Value:**	**$51,694,321.00**	**Pay App Work Completed:**	**10/31/2025**
Contractor Name:	**Fahs Construction Group Inc.**	**Amount Paid:**	**$47,915,897.00**	**Pay App Amount:**	**1,876,740.00**
Campus:	**Cornell - Ag&Life Sci.**	**Percent Paid:**	**92.7%**	**Pay App Submittal Date:**	**11/12/2025**
Description:	**Renovate Plant Science Buildin**	**Coordinator:**	**John Campbell**		
Construction Award Date:	**05/04/2023**	**Construction Manager:**	**LeChase Construction Services, LLC**		
End Date (projected):		**# of EEO Reports:**	**41**		**Approved**

Firm Id	Firm Name	Trade Code/Description	M/WBE	SDV	Start Date	End Date	Approved Plan Value	Payment Amount	Previously Paid	Total Paid to Date	Total % Paid
A0028	AAA Reinforcing LLC	157 - Structural Steel	WBE		10/1/2023	10/1/2024	230,000.00	0.00	195,980.00	195,980.00	85.21%
A0080	Academy Energy	200 - Electrical Suppl		SDV	9/1/2023	9/1/2025	60,000.00	0.00	0.00	0.00	0%
A0117	A & B Heritage Inc	211 - Signage	WBE		10/1/2025	12/1/2025	8,298.00	0.00	0.00	0.00	0%
A0127	AmBuild Supply, LLC	186 - Misc Site Subs		SDV	8/1/2025	12/1/2025	2,724.00	2,723.00	0.00	2,723.00	99.96%
A0140	Avarus Solutions, LLC	161 - Misc. Constructi	WBE		10/1/2024	12/1/2025	420,315.00	40,144.00	313,871.00	398,002.00	94.69%
B6389	Bonded Building Materials, Inc.	208 - Roofing Supplier	WBE		3/1/2025	11/1/2025	168,000.00	0.00	229,071.00	230,071.00	136.95%
C6333	Commercial Material Services Inc	142 - Doors & Hardware	WBE		9/1/2023	12/1/2025	683,000.00	0.00	0.00	0.00	0%
D9675	Dyno Group Inc	254 - Firestopping	MBE		7/1/2024	12/1/2025	967,500.00	57,222.00	1,137,326.00	1,194,548.00	123.47%
H0050	Healthy Glass LLC	265 - Window Treatment	WBE		8/1/2025	12/1/2025	6,500.00	0.00	0.00	0.00	0%
I0002	Illuminating Expressions Distrib	266 - Lighting Supplie	WBE		10/1/2024	10/1/2025	329,940.00	99,171.00	477,303.00	576,474.00	174.72%
I6007	Interstate Steel Sales Inc.	157 - Structural Steel	WBE		12/1/2023	12/1/2024	30,000.00	0.00	29,134.00	29,134.00	97.11%
K4407	Kim Industries Inc	154 - Plumbing	MBE		9/1/2024	9/1/2025	193,000.00	9,646.00	155,532.00	182,405.00	94.51%
K4407	Kim Industries Inc	254 - Firestopping	MBE		10/1/2024	10/1/2025	126,500.00	0.00	87,853.00	121,583.00	96.11%
K8055	Ksp Painting of Syracuse, Ltd.	153 - Painting	WBE		3/1/2025	12/1/2025	504,000.00	44,365.00	143,641.00	263,801.00	52.34%
L9320	Lupini Construction, Inc.	190 - Concrete	WBE		6/1/2023	12/1/2025	2,019,000.00	12,901.00	1,757,974.00	1,921,526.00	95.17%
M0005	MAC Equipment, LLC	199 - Misc. Equipment	WBE		6/1/2023	7/1/2025	45,000.00	0.00	0.00	0.00	0%
M2102	Mechanical Testing Inc.	186 - Misc Site Subs	WBE		9/1/2025	1/1/2026	62,900.00	0.00	0.00	0.00	0%
R4060	Riccelli Trucking, Inc.	164 - Waste Transporte	WBE		6/1/2023	12/1/2025	60,000.00	0.00	61,434.00	64,401.00	107.34%
R4060	Riccelli Trucking, Inc.	164 - Waste Transporte	WBE		3/1/2025	11/1/2025	15,000.00	4,143.00	7,509.00	15,741.00	104.94%
R4244	Right Price Companies Inc	162 - Laboratory Equip	MBE		6/1/2025	12/1/2025	150,000.00	0.00	0.00	0.00	0%
R6354	Rommel Fence LLC	188 - Fencing	WBE		6/1/2023	12/1/2025	41,000.00	0.00	35,227.00	35,227.00	85.92%
S0021	The Stalwart Development Group L	170 - Asbestos Abateme	MBE		6/1/2023	12/1/2024	2,178,000.00	0.00	2,520,658.00	2,551,613.00	117.15%
S0028	Shamrock Portable Restrooms, LLC	267 - Porta John/Potty		SDV	6/1/2023	12/1/2025	18,000.00	2,754.00	16,661.00	19,415.00	107.86%

MWBE/SDVOB Subcontractors Report by Contract

Contract Number:	**D006822**	**Construction Award:**	**$47,339,000.00**	**Payment Application No.:**	**27**
Project Number:	**161026-04**	**Contract Value:**	**$51,694,321.00**	**Pay App Work Completed:**	**10/31/2025**
Contractor Name:	**Fahs Construction Group Inc.**	**Amount Paid:**	**$47,915,897.00**	**Pay App Amount:**	**1,876,740.00**
Campus:	**Cornell - Ag&Life Sci.**	**Percent Paid:**	**92.7%**	**Pay App Submittal Date:**	**11/12/2025**
Description:	**Renovate Plant Science Buildin**	**Coordinator:**	**John Campbell**		
Construction Award Date:	**05/04/2023**	**Construction Manager:**	**LeChase Construction Services, LLC**		
End Date (projected):		**# of EEO Reports:**	**41**		**Approved**

Firm Id	Firm Name	Trade Code/Description	M/WBE	SDV	Start Date	End Date	Approved Plan Value	Payment Amount	Previously Paid	Total Paid to Date	Total % Paid
T0013	Tony Baird Electronics, Inc	200 - Electrical Suppl	MBE	SDV	9/1/2023	9/1/2025	60,000.00	0.00	140,304.00	140,304.00	233.84%
T9415	Turtle & Hughes Inc.	200 - Electrical Suppl	WBE		9/1/2023	9/1/2025	180,000.00	0.00	379,091.00	379,091.00	210.61%
T9415	Turtle & Hughes Inc.	200 - Electrical Suppl	WBE		3/1/2024	9/1/2025	30,000.00	0.00	6,300.00	6,300.00	21%
Z4662	Ziske-Kraftwerks Inc	211 - Signage	WBE		10/1/2025	12/1/2025	173,514.00	0.00	0.00	0.00	0%
						Totals:	**8,762,191.00**	**273,069.00**	**7,694,869.00**	**8,328,339.00**	**95.05%**

GOAL PROGRESS

Construction Award	Contract Goal	Approved Goal	Approved Plan Amount	Total Paid to Date	Contract Goal Credit	Contract Goal Attainment	Approved Goal Attainment
$47,339,000.00							
MBE	**15%**	**7.76%**	**3,675,000.00**	**4,108,541.00**	**8.68%**	**(6.32)**	**0.92**
WBE	**15%**	**10.58%**	**5,006,467.00**	**3,837,259.00**	**8.11%**	**(6.89)**	**(2.47)**
MWBE	**30%**	**18.34%**	**8,681,467.00**	**7,945,800.00**	**16.79%**	**(13.21)**	**(1.55)**
SDVOB	**6%**	**0.3%**	**140,724.00**	**162,442.00**	**0.34%**	**(5.66)**	**0.04**

MWBE/SDVOB Subcontractors Report by Contract

Contract Number:	**D006822**	**Construction Award:**	**$47,339,000.00**	**Payment Application No.:**	**28**
Project Number:	**161026-04**	**Contract Value:**	**$51,694,321.00**	**Pay App Work Completed:**	**11/30/2025**
Contractor Name:	**Fahs Construction Group Inc.**	**Amount Paid:**	**$47,915,897.00**	**Pay App Amount:**	**1,391,584.00**
Campus:	**Cornell - Ag&Life Sci.**	**Percent Paid:**	**92.7%**	**Pay App Submittal Date:**	**12/09/2025**
Description:	**Renovate Plant Science Buildin**	**Coordinator:**	**John Campbell**		
Construction Award Date:	**05/04/2023**	**Construction Manager:**	**LeChase Construction Services, LLC**		
End Date (projected):		**# of EEO Reports:**	**41**		**Approved**

Firm Id	Firm Name	Trade Code/Description	M/WBE	SDV	Start Date	End Date	Approved Plan Value	Payment Amount	Previously Paid	Total Paid to Date	Total % Paid
A0028	AAA Reinforcing LLC	157 - Structural Steel	WBE		10/1/2023	10/1/2024	230,000.00	0.00	195,980.00	195,980.00	85.21%
A0080	Academy Energy	200 - Electrical Suppl		SDV	9/1/2023	9/1/2025	60,000.00	0.00	0.00	0.00	0%
A0117	A & B Heritage Inc	211 - Signage	WBE		10/1/2025	12/1/2025	8,298.00	0.00	0.00	0.00	0%
A0127	AmBuild Supply, LLC	186 - Misc Site Subs		SDV	8/1/2025	12/1/2025	2,724.00	0.00	2,723.00	2,723.00	99.96%
A0140	Avarus Solutions, LLC	161 - Misc. Constructi	WBE		10/1/2024	12/1/2025	420,315.00	27,208.00	354,015.00	398,002.00	94.69%
B6389	Bonded Building Materials, Inc.	208 - Roofing Supplier	WBE		3/1/2025	11/1/2025	168,000.00	0.00	229,071.00	230,071.00	136.95%
C6333	Commercial Material Services Inc	142 - Doors & Hardware	WBE		9/1/2023	12/1/2025	683,000.00	0.00	0.00	0.00	0%
D9675	Dyno Group Inc	254 - Firestopping	MBE		7/1/2024	12/1/2025	967,500.00	0.00	1,194,548.00	1,194,548.00	123.47%
H0050	Healthy Glass LLC	265 - Window Treatment	WBE		8/1/2025	12/1/2025	6,500.00	0.00	0.00	0.00	0%
I0002	Illuminating Expressions Distrib	266 - Lighting Supplie	WBE		10/1/2024	10/1/2025	329,940.00	0.00	576,474.00	576,474.00	174.72%
I6007	Interstate Steel Sales Inc.	157 - Structural Steel	WBE		12/1/2023	12/1/2024	30,000.00	0.00	29,134.00	29,134.00	97.11%
K4407	Kim Industries Inc	154 - Plumbing	MBE		9/1/2024	9/1/2025	193,000.00	0.00	165,178.00	182,405.00	94.51%
K4407	Kim Industries Inc	254 - Firestopping	MBE		10/1/2024	10/1/2025	126,500.00	0.00	87,853.00	121,583.00	96.11%
K8055	Ksp Painting of Syracuse, Ltd.	153 - Painting	WBE		3/1/2025	12/1/2025	504,000.00	33,425.00	188,006.00	263,801.00	52.34%
L9320	Lupini Construction, Inc.	190 - Concrete	WBE		6/1/2023	12/1/2025	2,019,000.00	0.00	1,770,875.00	1,921,526.00	95.17%
M0005	MAC Equipment, LLC	199 - Misc. Equipment	WBE		6/1/2023	7/1/2025	45,000.00	0.00	0.00	0.00	0%
M2102	Mechanical Testing Inc.	186 - Misc Site Subs	WBE		9/1/2025	1/1/2026	62,900.00	0.00	0.00	0.00	0%
R4060	Riccelli Trucking, Inc.	164 - Waste Transporte	WBE		6/1/2023	12/1/2025	60,000.00	0.00	61,434.00	64,401.00	107.34%
R4060	Riccelli Trucking, Inc.	164 - Waste Transporte	WBE		3/1/2025	11/1/2025	15,000.00	4,089.00	11,652.00	15,741.00	104.94%
R4244	Right Price Companies Inc	162 - Laboratory Equip	MBE		6/1/2025	12/1/2025	150,000.00	0.00	0.00	0.00	0%
R6354	Rommel Fence LLC	188 - Fencing	WBE		6/1/2023	12/1/2025	41,000.00	0.00	35,227.00	35,227.00	85.92%
S0021	The Stalwart Development Group L	170 - Asbestos Abateme	MBE		6/1/2023	12/1/2024	2,178,000.00	0.00	2,520,658.00	2,551,613.00	117.15%
S0028	Shamrock Portable Restrooms, LLC	267 - Porta John/Potty		SDV	6/1/2023	12/1/2025	18,000.00	0.00	19,415.00	19,415.00	107.86%

MWBE/SDVOB Subcontractors Report by Contract

Contract Number:	**D006822**	**Construction Award:**	**$47,339,000.00**	**Payment Application No.:**	**28**
Project Number:	**161026-04**	**Contract Value:**	**$51,694,321.00**	**Pay App Work Completed:**	**11/30/2025**
Contractor Name:	**Fahs Construction Group Inc.**	**Amount Paid:**	**$47,915,897.00**	**Pay App Amount:**	**1,391,584.00**
Campus:	**Cornell - Ag&Life Sci.**	**Percent Paid:**	**92.7%**	**Pay App Submittal Date:**	**12/09/2025**
Description:	**Renovate Plant Science Buildin**	**Coordinator:**	**John Campbell**		
Construction Award Date:	**05/04/2023**	**Construction Manager:**	**LeChase Construction Services, LLC**		
End Date (projected):		**# of EEO Reports:**	**41**		**Approved**

Firm Id	Firm Name	Trade Code/Description	M/WBE	SDV	Start Date	End Date	Approved Plan Value	Payment Amount	Previously Paid	Total Paid to Date	Total % Paid
T0013	Tony Baird Electronics, Inc	200 - Electrical Suppl	MBE	SDV	9/1/2023	9/1/2025	60,000.00	0.00	140,304.00	140,304.00	233.84%
T9415	Turtle & Hughes Inc.	200 - Electrical Suppl	WBE		9/1/2023	9/1/2025	180,000.00	0.00	379,091.00	379,091.00	210.61%
T9415	Turtle & Hughes Inc.	200 - Electrical Suppl	WBE		3/1/2024	9/1/2025	30,000.00	0.00	6,300.00	6,300.00	21%
Z4662	Ziske-Kraftwerks Inc	211 - Signage	WBE		10/1/2025	12/1/2025	173,514.00	0.00	0.00	0.00	0%
						Totals:	**8,762,191.00**	**64,722.00**	**7,967,938.00**	**8,328,339.00**	**95.05%**

GOAL PROGRESS

Construction Award	Contract Goal	Approved Goal	Approved Plan Amount	Total Paid to Date	Contract Goal Credit	Contract Goal Attainment	Approved Goal Attainment
$47,339,000.00							
MBE	**15%**	**7.76%**	**3,675,000.00**	**4,108,541.00**	**8.68%**	**(6.32)**	**0.92**
WBE	**15%**	**10.58%**	**5,006,467.00**	**3,901,981.00**	**8.24%**	**(6.76)**	**(2.34)**
MWBE	**30%**	**18.34%**	**8,681,467.00**	**8,010,522.00**	**16.92%**	**(13.08)**	**(1.42)**
SDVOB	**6%**	**0.3%**	**140,724.00**	**162,442.00**	**0.34%**	**(5.66)**	**0.04**

MWBE/SDVOB Subcontractors Report by Contract

Contract Number:	**D006822**	**Construction Award:**	**$47,339,000.00**	**Payment Application No.:**	**29**
Project Number:	**161026-04**	**Contract Value:**	**$51,694,321.00**	**Pay App Work Completed:**	**12/31/2025**
Contractor Name:	**Fahs Construction Group Inc.**	**Amount Paid:**	**$47,915,897.00**	**Pay App Amount:**	**502,540.00**
Campus:	**Cornell - Ag&Life Sci.**	**Percent Paid:**	**92.7%**	**Pay App Submittal Date:**	**01/09/2026**
Description:	**Renovate Plant Science Buildin**	**Coordinator:**			
Construction Award Date:	**05/04/2023**	**Construction Manager:**	**LeChase Construction Services, LLC**		
End Date (projected):		**# of EEO Reports:**	**41**		**Approved**

Firm Id	Firm Name	Trade Code/Description	M/WBE	SDV	Start Date	End Date	Approved Plan Value	Payment Amount	Previously Paid	Total Paid to Date	Total % Paid
A0028	AAA Reinforcing LLC	157 - Structural Steel	WBE		10/1/2023	10/1/2024	230,000.00	0.00	195,980.00	195,980.00	85.21%
A0080	Academy Energy	200 - Electrical Suppl		SDV	9/1/2023	9/1/2025	60,000.00	0.00	0.00	0.00	0%
A0117	A & B Heritage Inc	211 - Signage	WBE		10/1/2025	12/1/2025	8,298.00	0.00	0.00	0.00	0%
A0127	AmBuild Supply, LLC	186 - Misc Site Subs		SDV	8/1/2025	12/1/2025	2,724.00	0.00	2,723.00	2,723.00	99.96%
A0140	Avarus Solutions, LLC	161 - Misc. Constructi	WBE		10/1/2024	12/1/2025	420,315.00	16,779.00	381,223.00	398,002.00	94.69%
B6389	Bonded Building Materials, Inc.	208 - Roofing Supplier	WBE		3/1/2025	11/1/2025	168,000.00	1,000.00	229,071.00	230,071.00	136.95%
C6333	Commercial Material Services Inc	142 - Doors & Hardware	WBE		9/1/2023	12/1/2025	683,000.00	0.00	0.00	0.00	0%
D9675	Dyno Group Inc	254 - Firestopping	MBE		7/1/2024	12/1/2025	967,500.00	0.00	1,194,548.00	1,194,548.00	123.47%
H0050	Healthy Glass LLC	265 - Window Treatment	WBE		8/1/2025	12/1/2025	6,500.00	0.00	0.00	0.00	0%
I0002	Illuminating Expressions Distrib	266 - Lighting Supplie	WBE		10/1/2024	10/1/2025	329,940.00	0.00	576,474.00	576,474.00	174.72%
I6007	Interstate Steel Sales Inc.	157 - Structural Steel	WBE		12/1/2023	12/1/2024	30,000.00	0.00	29,134.00	29,134.00	97.11%
K4407	Kim Industries Inc	154 - Plumbing	MBE		9/1/2024	9/1/2025	193,000.00	17,227.00	165,178.00	182,405.00	94.51%
K4407	Kim Industries Inc	254 - Firestopping	MBE		10/1/2024	10/1/2025	126,500.00	33,730.00	87,853.00	121,583.00	96.11%
K8055	Ksp Painting of Syracuse, Ltd.	153 - Painting	WBE		3/1/2025	12/1/2025	504,000.00	42,370.00	221,431.00	263,801.00	52.34%
L9320	Lupini Construction, Inc.	190 - Concrete	WBE		6/1/2023	12/1/2025	2,019,000.00	150,651.00	1,770,875.00	1,921,526.00	95.17%
M0005	MAC Equipment, LLC	199 - Misc. Equipment	WBE		6/1/2023	7/1/2025	45,000.00	0.00	0.00	0.00	0%
M2102	Mechanical Testing Inc.	186 - Misc Site Subs	WBE		9/1/2025	1/1/2026	62,900.00	0.00	0.00	0.00	0%
R4060	Riccelli Trucking, Inc.	164 - Waste Transporte	WBE		6/1/2023	12/1/2025	60,000.00	2,967.00	61,434.00	64,401.00	107.34%
R4060	Riccelli Trucking, Inc.	164 - Waste Transporte	WBE		3/1/2025	11/1/2025	15,000.00	0.00	15,741.00	15,741.00	104.94%
R4244	Right Price Companies Inc	162 - Laboratory Equip	MBE		6/1/2025	12/1/2025	150,000.00	0.00	0.00	0.00	0%
R6354	Rommel Fence LLC	188 - Fencing	WBE		6/1/2023	12/1/2025	41,000.00	0.00	35,227.00	35,227.00	85.92%
S0021	The Stalwart Development Group L	170 - Asbestos Abateme	MBE		6/1/2023	12/1/2024	2,178,000.00	30,955.00	2,520,658.00	2,551,613.00	117.15%
S0028	Shamrock Portable Restrooms, LLC	267 - Porta John/Potty		SDV	6/1/2023	12/1/2025	18,000.00	0.00	19,415.00	19,415.00	107.86%

MWBE/SDVOB Subcontractors Report by Contract

Contract Number:	**D006822**	**Construction Award:**	**$47,339,000.00**	**Payment Application No.:**	**29**
Project Number:	**161026-04**	**Contract Value:**	**$51,694,321.00**	**Pay App Work Completed:**	**12/31/2025**
Contractor Name:	**Fahs Construction Group Inc.**	**Amount Paid:**	**$47,915,897.00**	**Pay App Amount:**	**502,540.00**
Campus:	**Cornell - Ag&Life Sci.**	**Percent Paid:**	**92.7%**	**Pay App Submittal Date:**	**01/09/2026**
Description:	**Renovate Plant Science Buildin**	**Coordinator:**			
Construction Award Date:	**05/04/2023**	**Construction Manager:**	**LeChase Construction Services, LLC**		
End Date (projected):		**# of EEO Reports:**	**41**		**Approved**

Firm Id	Firm Name	Trade Code/Description	M/WBE	SDV	Start Date	End Date	Approved Plan Value	Payment Amount	Previously Paid	Total Paid to Date	Total % Paid
T0013	Tony Baird Electronics, Inc	200 - Electrical Suppl	MBE	SDV	9/1/2023	9/1/2025	60,000.00	0.00	140,304.00	140,304.00	233.84%
T9415	Turtle & Hughes Inc.	200 - Electrical Suppl	WBE		9/1/2023	9/1/2025	180,000.00	0.00	379,091.00	379,091.00	210.61%
T9415	Turtle & Hughes Inc.	200 - Electrical Suppl	WBE		3/1/2024	9/1/2025	30,000.00	0.00	6,300.00	6,300.00	21%
Z4662	Ziske-Kraftwerks Inc	211 - Signage	WBE		10/1/2025	12/1/2025	173,514.00	0.00	0.00	0.00	0%
						Totals:	**8,762,191.00**	**295,679.00**	**8,032,660.00**	**8,328,339.00**	**95.05%**

GOAL PROGRESS

Construction Award	Contract Goal	Approved Goal	Approved Plan Amount	Total Paid to Date	Contract Goal Credit	Contract Goal Attainment	Approved Goal Attainment
$47,339,000.00							
MBE	**15%**	**7.76%**	**3,675,000.00**	**4,190,453.00**	**8.85%**	**(6.15)**	**1.09**
WBE	**15%**	**10.58%**	**5,006,467.00**	**4,115,748.00**	**8.69%**	**(6.31)**	**(1.89)**
MWBE	**30%**	**18.34%**	**8,681,467.00**	**8,306,201.00**	**17.54%**	**(12.46)**	**(0.80)**
SDVOB	**6%**	**0.3%**	**140,724.00**	**162,442.00**	**0.34%**	**(5.66)**	**0.04**

ATTACHMENT B

WORKFORCE UTILIZATION

WORKFORCE ETHNICITY BREAKDOWN - TOTAL EMPLOYEE WORKDAYS ON SITE BY CONTRACTOR

	Caucasian/White		Black/African American		Hispanic/Latino		Asian/Pacific Islander		Native American/Indigenous		Total Count
	Count	%	Count	%	Count	%	Count	%	Count	%	
Ajay Glass & Mirror Co., Inc.	18	94.7%		0.0%		0%	1	5%		0%	19
AJG Associates	8	100%		0%		0%		0%		0%	8
Avarus Solutions	7	88%	1	13%		0%		0%		0%	8
C&B Mechanical	6	100%		0%		0%		0%		0%	6
Crosby-Brownlie, Inc.	19	86.4%		0%	3	13.6%		0%		0%	22
Draperies Etc, Inc.	1	100%		0%		0%		0%		0%	1
Driscoll Masonry Restoration	4	100%		0%		0%		0%		0%	4
FAHS Construction Group	24	100.0%		0.0%		0%		0.0%		0%	24
GC Flooring	3	100%		0%		0%		0%		0%	3
J&A Plastering	5	71%	2	29%		0%		0%		0%	7
John C. Lowery, Inc.	28	100%		0%		0%		0%		0%	28
Kim Industries, Inc.	3	100%		0%		0%		0%		0%	3
KONE	6	100%		0%		0%		0%		0%	6
Kraftwerks	3	100%		0%		0%		0%		0%	3
KSP Painting of Syracuse, Ltd.	16	73%		0%		0%		0%	6	27%	22
Martino Tile	6	100%		0%		0%		0%		0%	6
Matco Electric	76	93.8%	5	6.2%		0%		0%		0%	81
North Central Mechanical, Inc.	13	100%		0%		0%		0%		0%	13
Patriot Sons USA, LLC	3	100%		0%		0%		0%		0%	3
R.W. Dake & Co.	9	100%		0%		0%		0%		0%	9
Raulli & Sons, Inc.	8	100.0%		0%		0%		0.0%		0%	8
Southern Tier Insulations	9	100%		0%		0%		0%		0%	9
SRI Fire Sprinkler	10	77%		0%	3	23%		0%		0%	13
Grand Total	**285**	**93.1%**	**8**	**2.6%**	**6**	**2.0%**	**1**	**0.3%**	**6**	**2.0%**	**306**

WORKFORCE ETHNICITY BREAKDOWN - HOURS WORKED ON SITE BY CONTRACTOR

	Caucasian/White		Black/African American		Hispanic/Latino		Asian/Pacific Islander		Native American/Indigenous		Total Count
	Count	%	Count	%	Count	%	Count	%	Count	%	
Ajay Glass & Mirror Co., Inc.	1188	98.0%		0.0%		0%	24	2%		0%	1212
AJG Associates	88	100%		0%		0%		0%		0%	88
Avarus Solutions	553	88%	72.25	12%		0%		0%		0%	625
C&B Mechanical	717	100%		0%		0%		0%		0%	717
Crosby-Brownlie, Inc.	2542	83.6%		0%	498	16.4%		0%		0%	3040
Draperies Etc, Inc.	7	100%		0%		0%		0%		0%	7
Driscoll Masonry Restoration	32	100%		0%		0%		0%		0%	32
FAHS Construction Group	641	100.0%		0.0%		0%		0%		0%	641
GC Flooring	24	100%		0%		0%		0%		0%	24
J&A Plastering	104	72%	41	28%		0%		0%		0%	145
John C. Lowery, Inc.	2600	100%		0%		0%		0%		0%	2600
Kim Industries, Inc.	18	100%		0%		0%		0%		0%	18
KONE	93	100%		0%		0%		0%		0%	93
Kraftwerks	24	100%		0%		0%		0%		0%	24
KSP Painting of Syracuse, Ltd.	919	55.8%		0%		0%		0%	727.5	44.2%	1647
Martino Tile	520	100%		0%		0%		0%		0%	520
Matco Electric	7725	91.6%	704	8.4%		0%		0%		0%	8429
North Central Mechanical, Inc.	948	100%		0%		0%		0%		0%	948
Patriot Sons USA, LLC	40	100%		0%		0%		0%		0%	40
R.W. Dake & Co.	216	100%		0%		0%		0%		0%	216
Raulli & Sons, Inc.	48	100.0%		0%		0%		0.0%		0%	48
Southern Tier Insulations	485	100%		0%		0%		0%		0%	485
SRI Fire Sprinkler	853	88%		0%	120	12%		0%		0%	973
Grand Total	**20383**	**90.3%**	**817.25**	**3.6%**	**618**	**2.7%**	**24**	**0.1%**	**727.5**	**3.2%**	**22570**
